Public Disclosure Authorized

Public Disclosure Copy

Road Maintenance (P082026)

LATIN AMERICA AND CARIBBEAN | Paraguay | Transport & ICT Global Practice |
IBRD/IDA | Specific Investment Loan | FY 2007 | Seq No: 24 | ARCHIVED on 30-Jun-2016 | ISR23947 |

Implementing Agencies: MOPC

Key Dates

Key Project Dates

Bank Approval Date:24-Aug-2006
Effectiveness Date:03-Jan-2008
Planned Mid Term Review Date:06-Sep-2011
Actual Mid-Term Review Date:29-Nov-2011
Original Closing Date:30-Jun-2012
Revised Closing Date:30-Jun-2016

Project Development Objectives

Project Development Objective (from Project Appraisal Document)
The project's development objective is to establish a sustainable road management strategy that ensures the upgrading and maintenance of the road network through a rational and balanced use of scarce resources.

Has the Project Development Objective been changed since Board Approval of the Project Objective?
No

Public Disclosure Authorized

Components

Name
Strengthening of Road Management and Strategic Planning:(Cost $6.51 M)
Improvement and Maintenance of Paved Road Network:(Cost $43.35 M)
Improvement and Maintenance of the Unpaved Road Network:(Cost $42.90 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
Overall Implementation Progress (IP)	Moderately Unsatisfactory	Moderately Unsatisfactory
Overall Risk Rating	Substantial	Substantial

Public Disclosure Copy

Public Disclosure Copy

Implementation Status and Key Decisions

The project will close June 30, 2016 with an expected 94% of the IBRD loan disbursed. The preparation of the ICR is underway and the document will be disclosed publicly by end November 2016. While the project did encounter significant delays - with closing date extensions totaling 4 years - most of the planned outputs have been delivered and achievement of PDO is rated as moderately satisfactory. The various activities which had not been completed at end December 2015 are under execution and will be completed by project closure or shortly after.

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	Moderate	Moderate
Macroeconomic	--	Moderate	Moderate
Sector Strategies and Policies	--	Substantial	Substantial
Technical Design of Project or Program	--	Moderate	Moderate
Institutional Capacity for Implementation and Sustainability	--	Substantial	Substantial
Fiduciary	--	Substantial	Substantial
Environment and Social	--	High	High
Stakeholders	--	Moderate	Moderate
Other	--	--	--
Overall	--	Substantial	Substantial

Results

Project Development Objective Indicators

▸ Road strategy and five year plan implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target

Value	No	Yes	Yes	Yes
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

Comments
Achieved. Road strategy as approved in December 2006 and the five year plan was prepared and is now under implementation. The strategy has helped increase the percentage of paved roads and improve the overall condition of the road network. MOPC is in a position to provide a new and updated five year plan based on inputs provided through the Project.

▸ Percentage compliance with standards of the length contracted (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	93.00	93.00	90.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved. Indicator was moved from intermediate to PDO indicator at the time of the January 2014 restructuring.

▸ Increased level of budget execution (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	68.00	74.00	83.00	75.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved. Indicator was introduced at the time of the January 2014 restructuring. Indicator covers all programs implemented by MOPC, not just those under the Project.

▸ Number of rural community beneficiaries with improved access to all weather roads in the three departments (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	33450.00	34100.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Indicator was introduced at the time of the January 2014 restructuring. Beneficiaries are defined as those living within 10 km of the improved roads under the Project.

▸ Percentage of users reporting satisfaction with the quality of the roads (San Pedro, Caazapa and Caaguazu road segments) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	--	--	--	--
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

Comments
The user satisfaction surveys have been carried out and results will be presented to the Government by June 30, 2016. After January 22, 2014 restructuring, this indicator only applies to beneficiaries in the three departments where non-paved roads are to be improved. The following were the reported levels of satisfaction: 7% good, 28% fair and 65% bad as a baseline.

◢ Percentage reporting roads to be in bad condition (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	--	--	0.00
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

▷ Percentage reporting roads to be in fair condition (Percentage, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	--	--	50.00
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

Overall Comments
The user surveys which will provide the information for the last indicator are underway. Final results are expected to be included in the Implementation Completion Report. Preliminary information shows that the user satisfaction is high in the three departments where the unpaved network was improved.

Intermediate Results Indicators

▸ Component 1 - Creation of Road Strategic Planning Unit (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No Unit	DPV created, operational, equipped and trained	DPV created, operational, equipped and trained	DPV created, operational, equipped and trained
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved. DPV unit is up and running and has adequate funding for equipment and personnel. Enabling measure was taken in February 2007 prior to loan effectiveness.

▸ Component 1 - Number of law, decrees and regulations related to the project enacted (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	5.00	2.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved. The completed legislation is as follows: Transit and Road Safety Law passed in 2014; Road Classification Law passed in 2016; creation of the DPV in MOPC by decree in February 2007; toll revenue ministerial directive (source of funding for road maintenance) passed; and ministerial directive to create the transparency department, DTPC, in February 2007.

▸ Component 1 - Programming and follow-up of the result-based management and budget implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Non-existent	Completed. Pilot program for results based management budget is being implemented. A report is issued twice a year to MEF.	Completed. Pilot program for results based management budget is being implemented. A report is issued twice a year to MEF.	Report on execution of budget for results
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved. A results-based budgeting system for the sector in in place and functional. This provides the basis for regular semi-annual reports.

▸ Component 1 - Strategy of Internal and external communication on road maintenance implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No strategy	Communications plan prepared and under implementation. Annual Progress Report from the Minister published. Monitoring Tool for Project Execution developed and implemented	Communications plan prepared and under implementation. Annual Progress Report from the Minister published. Monitoring Tool for Project Execution developed and implemented	Communications plan prepared and implemented implementation
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Achieved with delay. Strategy was prepared and is now under implementation since 2014. Generally more information is being made publicly available– such as on status of projects under execution – and this owes much to the IGAP.

▸ Component 2 - Km of road networked maintained under level of service (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	624.70	625.00	624.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Mostly achieved. Target was modified during the January 2014 restructuring so that the indicator only covers roads improved and maintained under the Project. Only 3 out of the original 4 GMANs contracts to be funded by the Project went forward (GMANs 2 was cancelled). There were time and cost overruns experienced on only one contract, GMANs 5. It was noted that 629 km were being maintained under levels of service under a parallel program funded by IDB.

Public Disclosure Copy

▸ Component 2- Master plan for optimization of roads toll collection developed and implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	Outdated toll collection system with 16 stations	Modern integral toll collection system underway (11 toll stations). 3 toll with significant progress between 80-90%. Remaining stations under construction with progress between 20-60%	Modern integral toll collection system underway	Modern integral toll collection system built and equipped for 11 stations
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments

Achieved. Modern integrated toll system in place with 11 stations representing a significant improvement in terms of both user service and revenue generation compared to ex ante status, which had 16 stations.

▸ Component 2- Road monitoring system implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	System contracted and under implementation. 1,955 Km of paved roads and 5,000 km of unpaved roads surveyed. 15,786 km non paved roads inventoried.	System contracted and under implementation.	System established
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments

Partially achieved with delay. System was established under the Project, being effectively utilized to measure compliance with the Road Strategy. A system of regular and permanent traffic counting is now in place, starting from 2014. . All paved network is part of the inventory and 50% of the unpaved network.

Public Disclosure Copy

Public Disclosure Copy

▸ Component 3 - Km of Unpaved Road Network Improved (Kilometers, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	115.00	115.00	140.00
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

Comments

Achieved with delay. Target was changed during the January 2014 restructuring to cover only roads to be improved under the funding of the Project. The improvements include a number of bridges which are not evaluated separately. A number of the works contracts suffered from time and cost overruns.Final number will be provided by the MOPC by August 15.

▸ Component 3- Indigenous Peoples Plan prepared and implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	IPP prepared.	Ongoing Construction	IPP prepared and implemented with 3 multi-use community centers
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments

Partially achieved with significant delay. 3 plans were prepared to be implemented in each of the three departments. Implementation was seriously delayed and plans were revised in 2011 with some components going forward. The construction of multi-use community centers for each department did not start until early 2016 however. The latter was significantly delayed and which was the primary motivation for the final extension of the closing date to June 30, 2016.

▸ Component 3- Maintenance system for unpaved roads is established through micro-enterprises in selected departments (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	6	6	10
Date	01-May-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments

Partly achieved. 6 micro-enterprises had been created at the time of the January 2014 restructuring when this indicator was added. No further micro-enterprises were created before the end of the Project because of budget limitations.

Public Disclosure Copy

Public Disclosure Copy

▸ Component 3- Vehicle operating cost-truck: San Pedro, Caazapa, Caaguazu (Guarani per veh-km) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	--	--	10368.00	--
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments

Expected to be Achieved. Target VOC were significantly reduced as part of the January 2014 restructuring based on revised, actual data for 2013 as follows:. 11483 (San Pedro), 11283 (Caazapa) and 11360 (Caaguazu). Final actual for Vehicle Operating Cost will be confirmed by the MOPC by project closing. The average vehicle operating cost for a large truck is reported as 10, 367.74 country wide. The actual breakdown by department is pending but based on the estimates for the country the target has been met.

◢ Vehicle operating cost-truck: Caazapa (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	17885.74	--	--	10496.92
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

▹ Vehicle operating cost-truck: Caaguazu (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	18324.46	--	--	10568.70
Date	01-Jan-2008	02-Oct-2015	02-Oct-2015	31-Dec-2015

◢ Vehicle operating cost-truck: San Pedro (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	18149.23	--	--	10682.36
Date	02-Jan-2012	02-Oct-2015	02-Oct-2015	31-Dec-2015

Public Disclosure Copy

Public Disclosure Copy

▸ Component 3- Number of Public Transport Vehicles in San Pedro, Caazapá and Caaguazú Road Segments (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	34.00	--	--	42.00
Date	--	--	--	30-Jun-2016

Comments
Target was reduced during January 2014 restructuring. Data unavailable at project closure, but is expected as part of the Implementation Completion Report.

▸ Roads rehabilitated, Non-rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	624.00	625.00	624.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

▸ Roads rehabilitated, Rural (Kilometers, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	115.00	115.00	140.00
Date	01-Jan-2008	02-Oct-2015	25-May-2016	31-Dec-2015

Comments
Target is to be completed and reported on by June 30, 2016.

Overall Comments
Indicators with pending data will be completed by July 30, 2016.

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed


Public Disclosure Copy

P082026	IBRD-74060	Effective	USD	74.00	74.00	0.00	69.18	4.82	93%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P082026	IBRD-74060	Effective	24-Aug-2006	13-Oct-2006	03-Jan-2008	30-Jun-2012	30-Jun-2016

Cumulative Disbursements

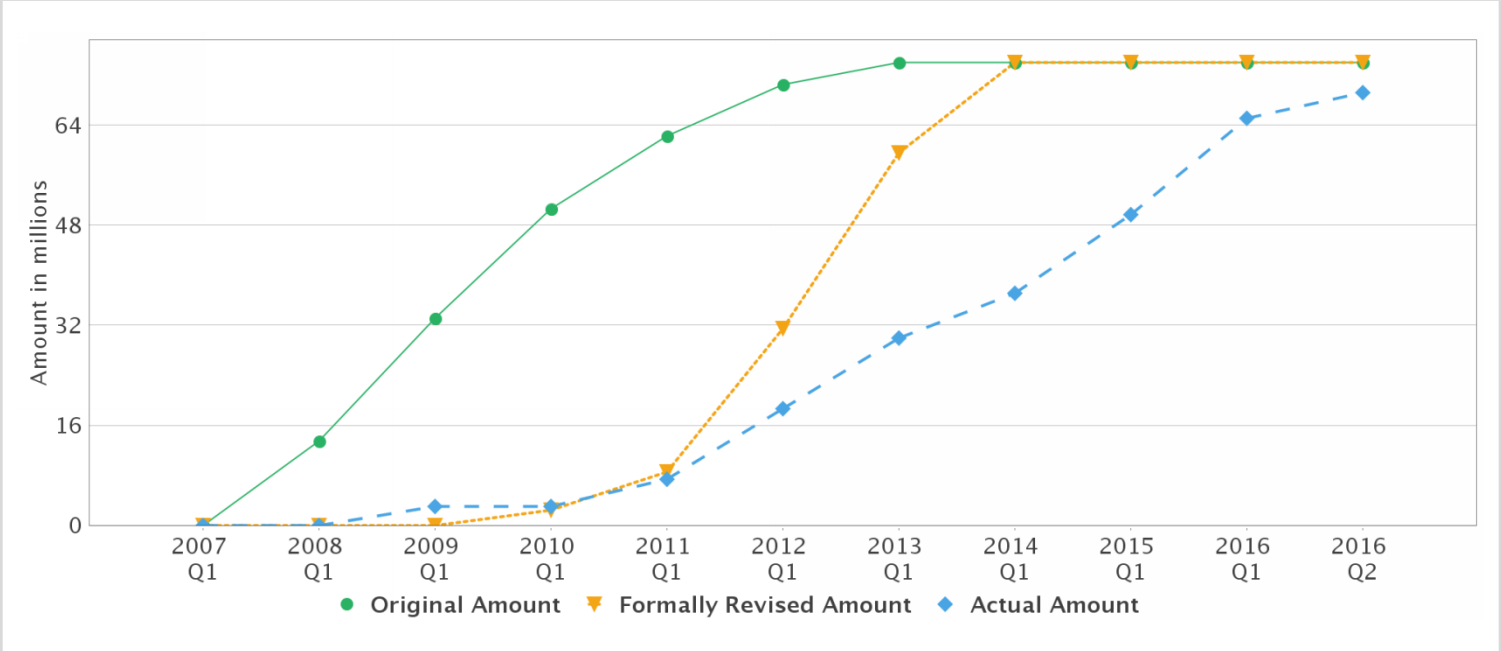

Restructuring History

Level Approved on 11-Jun-2012 ,Level Approved on 28-Mar-2013 ,Level 2 Approved on 03-Feb-2014 ,Level 2 Approved on 27-Jun-2015 ,Level 2 Approved on 28-Dec-2015

Related Project(s)

There are no related projects.
